

Localized Spot Fixes will be marked out by the contractor and completed prior to crack sealing on 5/8 through 5/19. No Parking signs will be placed 36 to 72 hours prior to start of work in each spot fix area.


Crack Sealing will be completed on the project roads noted in the maps between 6/8 and 6/12

Residents should not park on the street in the areas noted for crack sealing on that day, or if "No Parking" signs are present.

Updates or delays will be posted to the project page.

Legend

— 2026 Crack Seal

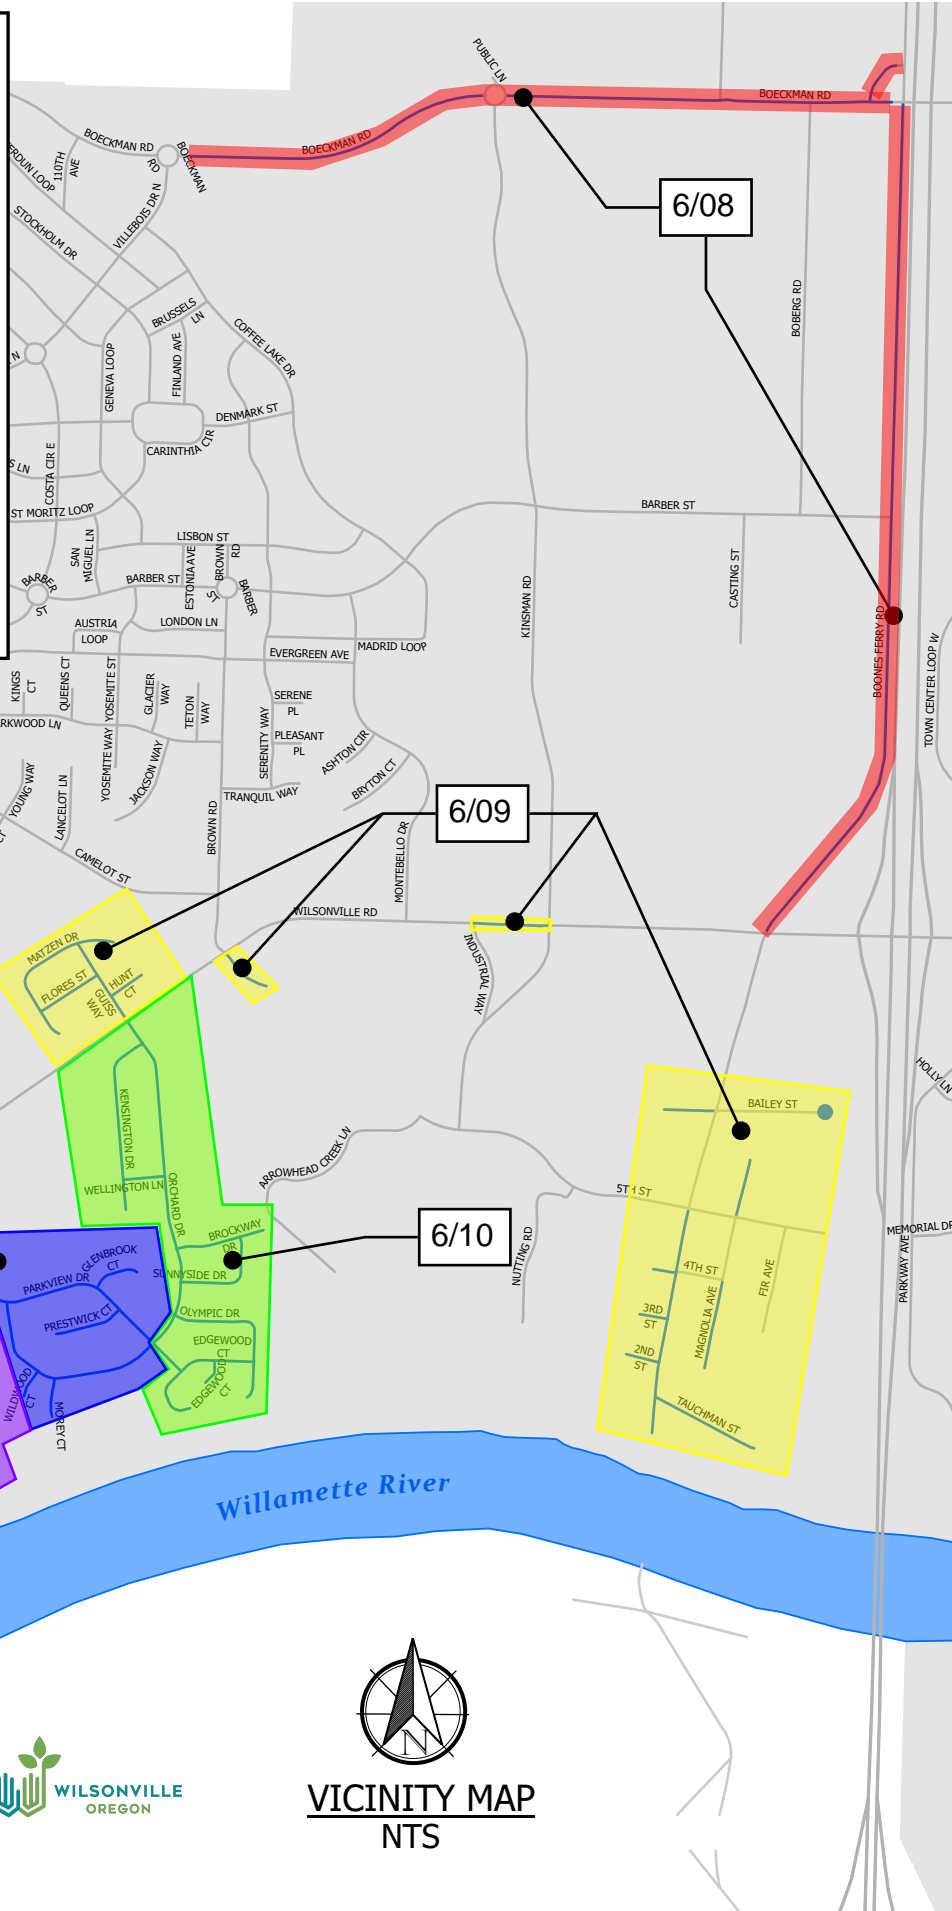

VICINITY MAP
NTS

ITEM#	TASK	LEAD	START	END	DAYS	% DONE	WORK DAYS	Week 1 8 Jun 2026							Week 2 15 Jun 2026				
								8	9	10	11	12	13	14	15	16	17	18	
								M	T	W	T	F	S	S	M	T	W	T	
1	BOECKMAN RD	CR Contracting	Mon 6/08/26	Mon 6/08/26	1	0%	1	█											
2	MATZEN DR	CR Contracting	Tue 6/09/26	Tue 6/09/26	1	0%	1		█										
2	FLORES ST	CR Contracting	Tue 6/09/26	Tue 6/09/26	1	0%	1		█										
2	GUISS WAY	CR Contracting	Tue 6/09/26	Tue 6/09/26	1	0%	1		█										
2	HUNT CT	CR Contracting	Tue 6/09/26	Tue 6/09/26	1	0%	1		█										
2	BROWN RD	CR Contracting	Tue 6/09/26	Tue 6/09/26	1	0%	1		█										
2	WILSONVILLE RD	CR Contracting	Tue 6/09/26	Tue 6/09/26	1	0%	1		█										
2	BAILY ST	CR Contracting	Tue 6/09/26	Tue 6/09/26	1	0%	1		█										
2	BOECKMAN RD	CR Contracting	Tue 6/09/26	Tue 6/09/26	1	0%	1		█										
2	MAGNOLIA AVE	CR Contracting	Tue 6/09/26	Tue 6/09/26	1	0%	1		█										
2	TAUCHMAN ST	CR Contracting	Tue 6/09/26	Tue 6/09/26	1	0%	1		█										
2	3RD ST	CR Contracting	Tue 6/09/26	Tue 6/09/26	1	0%	1		█										
2	2ND ST	CR Contracting	Tue 6/09/26	Tue 6/09/26	1	0%	1		█										
3	KENSINGTON DR	CR Contracting	Wed 6/10/26	Wed 6/10/26	1	0%	1			█									
3	WELLINTON LN	CR Contracting	Wed 6/10/26	Wed 6/10/26	1	0%	1			█									
3	ORCHARD DR	CR Contracting	Wed 6/10/26	Wed 6/10/26	1	0%	1			█									
3	BROCKWAY DR	CR Contracting	Wed 6/10/26	Wed 6/10/26	1	0%	1			█									
3	SUNNYSIDE DR	CR Contracting	Wed 6/10/26	Wed 6/10/26	1	0%	1			█									
3	OLYMPIC DR	CR Contracting	Wed 6/10/26	Wed 6/10/26	1	0%	1			█									
3	EDGEWOOD CT	CR Contracting	Wed 6/10/26	Wed 6/10/26	1	0%	1			█									
4	WILLAMETTE WAY	CR Contracting	Thu 6/11/26	Thu 6/11/26	1	0%	1				█								
4	CHANTILLY	CR Contracting	Thu 6/11/26	Thu 6/11/26	1	0%	1				█								
4	CHURCHILL	CR Contracting	Thu 6/11/26	Thu 6/11/26	1	0%	1				█								
4	PARKVIEW DR	CR Contracting	Thu 6/11/26	Thu 6/11/26	1	0%	1				█								
4	GLENNBROOK CT	CR Contracting	Thu 6/11/26	Thu 6/11/26	1	0%	1				█								
4	PRESTWICK CT	CR Contracting	Thu 6/11/26	Thu 6/11/26	1	0%	1				█								
4	WILDWOOD CT	CR Contracting	Thu 6/11/26	Thu 6/11/26	1	0%	1				█								
4	MOREY CT	CR Contracting	Thu 6/11/26	Thu 6/11/26	1	0%	1				█								
4	ORCHARD DR	CR Contracting	Thu 6/11/26	Thu 6/11/26	1	0%	1				█								
5	JAMAICA	CR Contracting	Fri 6/12/26	Fri 6/12/26	1	0%	1					█							
5	PREAKNESS	CR Contracting	Fri 6/12/26	Fri 6/12/26	1	0%	1					█							
5	PAULINA CT	CR Contracting	Fri 6/12/26	Fri 6/12/26	1	0%	1					█							
5	PAULINA DR	CR Contracting	Fri 6/12/26	Fri 6/12/26	1	0%	1					█							
5	CHAMPOEG DR	CR Contracting	Fri 6/12/26	Fri 6/12/26	1	0%	1					█							
5	CHAMPOEG CT	CR Contracting	Fri 6/12/26	Fri 6/12/26	1	0%	1					█							
5	MCKENZIE CT	CR Contracting	Fri 6/12/26	Fri 6/12/26	1	0%	1					█							
5	BELNAP CT	CR Contracting	Fri 6/12/26	Fri 6/12/26	1	0%	1					█							
5	FRENCH GLENN CT	CR Contracting	Fri 6/12/26	Fri 6/12/26	1	0%	1					█							
5	WILLAMTTE WAY	CR Contracting	Fri 6/12/26	Fri 6/12/26	1	0%	1					█							
